

No work is to be done before this matter is finalized and a "Change Order" is issued. This copy to remain with your office. Do not return. Contractor to submit signed letter with price including cost breakdown and change (if any) to construction schedule. Authority having Jurisdiction shall advise of any objections.

**TO: QUOREX CONSTRUCTION SERVICES LTD.**  
1630A 8th Avenue,  
Regina, SK S4R 1E5

**RE: AURORA FOOD STORE**  
2000 ANAQUOD ROAD  
REGINA, SK  
Commission No. 2445

**DATE:** October 15, 2025

**PAGES:** 2 (including cover)

**RE: Rolling Shutters HSS**

## 1.0 STRUCTURAL

- .1 Refer to attached Structural PCN S2, dated October 15, 2025 (1 page text)


## 2.0 ARCHITECTURAL

- .1 Install steel angle and HSS to suite Pharmacy security grilles.  
Orientation of north baseplate to face westward, located below steel stud wall.
- .2 Frame steel studs / wood blocking to suite.  
Exposed sides to be finished with gypsum board. Refer to Décor for finishes.
- .3 Window #W12 rough opening size may reduce in width to accommodate framing.

### Distribution:

Sobeys Inc. – Jeff Craig  
Sobeys Inc. – Shanwen Hsu  
Quorex Construction Services Ltd. – Chris Walbaum  
Quorex Construction Services Ltd. – Dustin Williamson  
Lavergne Draward & Associates Inc. – Charles Koop  
CGM Engineering – Justin Albo  
CGM Engineering – Tony Mitousis  
CGM Engineering – Brendan Simpson

jeff.craig@sobeys.com  
shanwen.hsu@sobeys.com  
c.walbaum@quorex.ca  
d.williamson@quorex.ca  
ckoop@ldaeng.ca  
justin\_albo@cgmeng.ca  
tony\_mitousis@cgmeng.ca  
brendan\_simpson@cgmeng.ca

  
Principal  
Kevin Fawley, SAA MRAIC

**Project Name: Aurora Food Store**

**Contractor: Quorex**

## Proposed Change Notice

Pursuant to the conditions of the Present Contract, the following items are proposed changes to the work for the above project. Submit cost of changes, including all sub-contract quotations, as additions or deductions to the Contract Price. Show a breakdown of cost for all labour, material, equipment and services required to complete the work described. No work shall proceed until formal approval is provided for the work.


**Project No.: 24739**

**Date: October 15, 2025**

**Item/Reference Instigation and Description**

**Item # 1 Rolling shutter end supports**  
**Instigation: Design Continuation**  
**Reference: SD# 049 R1 Rolling Shutter**

- a) At South end of shutter, provide L102x102x4.8 at full height required by shutter welded to HSS column South of GL E.
- b) At North end of shutter provide steel HSS 76x76x6.4 c/w slip connection to underside of beam above. Base plate to be ½"x3½"x12" c/w 2-¾"Ø Hilti Hit-Hy 200 4" embedment.

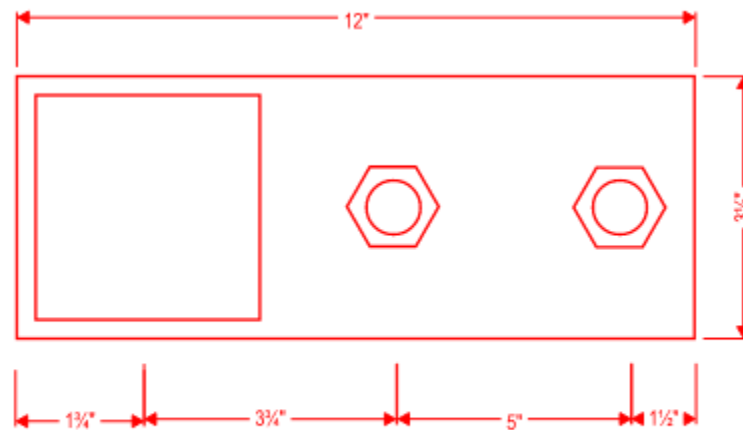

GC to coordinate dimensions and locations with architectural drawings to ensure structural components are kept within stud walls. GC to coordinate with roller shutter shop drawings to ensure structure is provided where required by roller shutter shop drawings.
